



TENNESSEE DEPARTMENT OF TRANSPORTATION
EROSION PREVENTION/SEDIMENT CONTROL
INSPECTION REPORT

TDOT EPSC INSPECTION FORM Rev. Feb 2010

Reason For Inspection: 1st Weekly

2nd Weekly

DATE: 2.16.12

State Route (SR) / US Route or Road Name and Description: Wolf River Blvd.			Are corrective actions required by this inspection report (Y/N): *		
County(ies): Shelby	TDOT PIN: 101615	NPDES Permit (NOC) #: TNR153299	Number of New Corrective Actions: 0	Number of Recurring Corrective Actions: 0	Number of New Sediment Releases: 0
TDOT Construction No.: 7994-1535-54	TDOT Contract No.:	Contractor: Acuff Enterprises Inc.			

I certify, under penalty of law that this document and all attachments were prepared under my direction or supervision in accordance with a system designed to assure that qualified personnel properly gathered and evaluated information presented. Based on my inquiry of the person or persons who manage the system, or those persons directly responsible for gathering the information, I certify that inspections of storm water discharge points (outfalls) and of erosion and sediment controls have been performed as recorded in the table above. I certify that erosion and sediment controls in the drainage area of the identified outfall where installed as planned and designed in working order as recorded in the table above. I am aware that there are significant penalties for submitting false information, including the possibility of fine and imprisonment for knowing violations.	COG EPSC Inspector: Gerald "Jerry" Stanfill	Signature:
	Contractor EPSC Inspectors: Tom Acuff and/or Steve Ballard	Signature:
	COG EPSC Project Manager: Timothy Bierz	Signature:

TDOT EPSC Inspection Weekly Rainfall Data Log

Date	Day of Week	Predicted Precipitation (%)	Rainfall Gauge 1 (in)	Rainfall Gauge 2 (in)	Rainfall Gauge 3 (in)	Rainfall Gauge 4 (in)	Rainfall Gauge 5 (in)	Rainfall Gauge 6 (in)	Duration (hr)	TDOT/Contractor Agrees with Inspection Report: NO or YES If No, explain and initial:
	Sunday				N/A	N/A	N/A	N/A		
2.13.12	Monday	100	0	0	N/A	N/A	N/A	N/A		
2.14.12	Tuesday	20			N/A	N/A	N/A	N/A		
2.15.12	Wednesday	50			N/A	N/A	N/A	N/A		
2.16.12	Thursday	10	0.65	0.60	N/A	N/A	N/A	N/A	12	
2.17.12	Friday	20			N/A	N/A	N/A	N/A		
2.18.12	Saturday	80			N/A	N/A	N/A	N/A		
2.19.12	Sunday	10			N/A	N/A	N/A	N/A		
	Monday				N/A	N/A	N/A	N/A		

(Additional pages may be attached, if needed)

Predicted Precipitation Source: www.weather.com

Page 1 of 7

* TOO WET TO WORK CONDITIONS

State/US Route or Road Name: Wolf River Blvd.TDOT Construction No.: 79954-3537-54

TDOT Contract No.: _____

Date 2/16/2012

Outfall Name or Station No.	Rain Gage No.	Approx. Station No. From / To	LT, RT or Centerline	Date Last Disturbed	Date of Stabilization and Code T = Temp. P = Perm.	Existing EPSC Control Measure Codes*	Current Condition Codes*	Corrective Action(s) or Comments
1	1	14+14	LT	2/13/2012		22,35	FM,W	Monitoring outfall.
1A	1	21+50	RT	2/9/2012		41	FM,W	Const. of RCBC Pedestrian Underpass in progress. No activity during inspection.
1B	1	22+00	RT	1/30/2011		35	FM,W	Install two RSS's. See photo
1C	1	21+00	LT	11/7/2011	T = 10-6-11	12,15,33,35	S,W	Temp. stable.
2A	1	33+50	LT,CL	1/20/2012		12,15,16	S,W	Temp. stable.
2B	1	35+50	LT	2/13/2012		16,24	FM,W	Weekly cleaning for stream crossing required, until further notice.
3	1	34+50	LT	10/27/2011		16	FM,W	Outfall slopes north of temp. stream crossing are showing signs of failure.
4	1	40+00	RT	12/12/2011	T = 10-24-11	15,16,43	S,W	Temp. stable.
5A	1	49+00	RT	2/9/2012		16,33	FM,W	Monitoring temp. BMP's.
5B	1	50+00	RT	2/9/2012		9,16,33	FM,W	Monitoring temp. BMP's.

EROSION AND SEDIMENT CONTROL MEASURE CODES

1 Temporary Silt Fence / Filter Barrier	15 Temporary seeding with Mulch	29 Excess Dirt Removed from Rdwy. Daily
2 Temporary Diversion Berm or Ditch	16 Temporary Mulch	30 Haul Roads Dampened for Dust Control
3 Temporary Slope Drain	17 Erosion Control Blanket	31 Ditch Liner
4 Rock Check Dams	18 Flexible Channel Liner	32 Rock Silt Screen
5 Brush Barrier	19 Catch Basin / Storm Inlet Protection	33 Temporary Silt Fence with Backing
6 Sediment Removal	20 Riprap Outlet Structure	34 Enhanced Silt Fence
7 Straw Bale Check	21 Riprap Energy / Velocity Dissipater	35 Sediment Tube
8 Sand Bags	22 Curb, Gutter, or Storm Sewer Protection	36 Sediment Dam
9 Sediment Trap / Basin	23 Temporary at Construction Exit / Entrance	37 Concrete Washout, other pollution Issues
10 Temp Sediment Filter Bag / Dewatering	24 Temporary Stream Crossing	38 Berm (soil, riprap, rock)
11 Polyethylene Sheeting	25 Turbidity Barrier / Silt Boom	39 Gabion
12 Machined Rip Rap	26 Temporary Stream Diversion	40 Sheet Piling
13 Geotextile	27 Preserve Natural Resource / Buffer Zone	41 Haul Road
14 Permanent Seeding with Mulch or Sod	28 Mineral Aggregate Base on Subgrade	42 Bridge Construction
		43 Stream Realignment

CONDITION CODES

M	Maintenance
U	Upgrade Needed (Failure Noted)
R	Replacement Needed
FM	Future Maintenance
C	Cleaning Needed
I	Increase Measures
W	Too Wet to Work Conditions
RO	Repeat Occurrence
SR	Sediment Release
FS	Final Stabilized
S	Stable (No Action Needed)
CM	Corrections currently being made

Other (O#1): _____

Other (O#2): _____

Other (O#3): _____

State/US Route or Road Name: Wolf River Blvd.TDOT Construction No.: 79954-3537-54

TDOT Contract No.: _____

Date 2/16/2012

Outfall Name or Station No.	Rain Gage No.	Approx. Station No. From / To	LT, RT or Centerline	Date Last Disturbed	Date of Stabilization and Code T = Temp. P = Perm.	Existing EPSC Control Measure Codes*	Current Condition Codes*	Corrective Action(s) or Comments
5C	1	44+00	LT	2/13/2012		16,24,33	FM,W	Weekly cleaning for stream crossing required.
6	1	56+00	LT	2/13/2012			FM,W	Activity around and in pond during inspection. Monitoring BMP's
7	1	60+00	RT	10/24/2011		16, 33	S,W	Temp. stable.
8A	1	73+00	RT	2/13/2012		16,24,42	FM,W	Weekly cleaning for stream crossing will be required, until further notice.
8B	2	75+50	RT	9/29/2011		16,35,41	S,W	Temp. stable.
8C	1	71+00	LT	2/13/2012		16,35,42	FM,W	Bridge 2, Abutment 1 rip rap continues to be installed along bank slopes.
8D	2	75+50	LT	2/9/2012	P = 2-2-12 riprap installed at Bridge 2, East Bank	12,16,35,42	FM,W	Monitoring temp. BMP's north of rip rap in place at bridge 2 east bank.
8E	1	71+50	LT, RT or CL	2/13/2012		12	FM,W	Rip Rap being installed under Bridge as per plans during inspection.
9A	2	80+00	RT	9/29/2011	T = 10-3-11	6,15,33,35	S,W	Temp. stable.
9B	2	80+00	LT	9/29/2011	T = 10-3-11	15,16,17,,35	S,W	Temp. stable.

EROSION AND SEDIMENT CONTROL MEASURE CODES

1 Temporary Silt Fence / Filter Barrier	15 Temporary Seeding with Mulch
2 Temporary Diversion Berm or Ditch	16 Temporary Mulch
3 Temporary Slope Drain	17 Erosion Control Blanket
4 Rock Check Dams	18 Flexible Channel Liner
5 Brush Barrier	19 Catch Basin / Storm Inlet Protection
6 Sediment Removal	20 Riprap Outlet Structure
7 Straw Bale Check	21 Riprap Energy / Velocity Dissipater
8 Sand Bags	22 Curb, Gutter, or Storm Sewer Protection
9 Sediment Trap / Basin	23 Temporary at Construction Exit / Entrance
10 Temp Sediment Filter Bag / Dewatering	24 Temporary Stream Crossing
11 Polyethylene Sheeting	25 Turbidity Barrier / Silt Boom
12 Machined Rip Rap	26 Temporary Stream Diversion
13 Geotextile	27 Preserve Natural Resource / Buffer Zone
14 Permanent Seeding with Mulch or Sod	28 Mineral Aggregate Base on Subgrade

29 Excess Dirt Removed from Rdwy. Daily
30 Haul Roads Dampened for Dust Control
31 Ditch Liner
32 Rock Silt Screen
33 Temporary Silt Fence with Backing
34 Enhanced Silt Fence
35 Sediment Tube
36 Sediment Dam
37 Concrete Washout, other pollution Issues
38 Berm (soil, riprap, rock)
39 Gabion
40 Sheet Piling
41 Haul Road
42 Bridge Construction

CONDITION CODES

M Maintenance
U Upgrade Needed (Failure Noted)
R Replacement Needed
FM Future Maintenance
C Cleaning Needed
I Increase Measures
W Too Wet to Work Conditions
RO Repeat Occurrence
SR Sediment Release
FS Final Stabilized
S Stable (No Action Needed)
CM Corrections currently being made

Other (O#1): _____
 Other (O#2): _____
 Other (O#3): _____

State/US Route or Road Name: Wolf River Blvd.TDOT Construction No.: 79954-3537-54

TDOT Contract No.: _____

Date 2/16/2012

Outfall Name or Station No.	Rain Gage No.	Approx. Station No. From / To	LT, RT or Centerline	Date Last Disturbed	Date of Stabilization and Code T = Temp. P = Perm.	Existing EPSC Control Measure Codes*	Current Condition Codes*	Corrective Action(s) or Comments
9C	2	79+50	LT	9/29/2011	T = 10-03-11	15,16,20,33	S,W	Temp. stable.
10A	2	85+00	RT	9/29/2011		15,16,35,41	FM,W	Areas need to be temp. stabilized. See photo
10B	2	85+00	RT	9/29/2011		15,16,35,41	FM,W	Areas need to be temp. stabilized. See photo
10C	2	85+50	LT	11/14/2011		15,16,35,41	FM,W	Areas need to be temp. stabilized.
10D	2	84+50	LT	1/6/2012		15,16,35,41	FM,W	Monitoring temp. BMP's.
11A	2	92+50	RT	11/14/2011		35,41	FM,W	Areas need to be temp. stabilized. See photo
11B	2	92+50	LT	1/6/2012		10,32,35,41	FM,W	Monitoring temp. BMP's.
11C	2	92+00	LT	10/6/2011		10,32,35,41	FM,W	Monitoring temp. BMP's.
	1	11+28	LT	2/13/2012		19,35	FM,W	Daily cleaning is required, until further notice.
	1	13+40	RT	2/13/2012		23,29,30	FM,W	Daily cleaning will be required, until further notice.
	1	107+75	CL	2/13/2012		23,29,30	FM,W	Daily cleaning will be required, until further notice.

EROSION AND SEDIMENT CONTROL MEASURE CODES

1 Temporary Silt Fence / Filter Barrier	15 Temporary Seeding with Mulch	29 Excess Dirt Removed from Rdwy. Daily
2 Temporary Diversion Berm or Ditch	16 Temporary Mulch	30 Haul Roads Dampened for Dust Control
3 Temporary Slope Drain	17 Erosion Control Blanket	31 Ditch Liner
4 Rock Check Dams	18 Flexible Channel Liner	32 Rock Silt Screen
5 Brush Barrier	19 Catch Basin / Storm Inlet Protection	33 Temporary Silt Fence with Backing
6 Sediment Removal	20 Riprap Outlet Structure	34 Enhanced Silt Fence
7 Straw Bale Check	21 Riprap Energy / Velocity Dissipater	35 Sediment Tube
8 Sand Bags	22 Curb, Gutter, or Storm Sewer Protection	36 Sediment Dam
9 Sediment Trap / Basin	23 Temporary at Construction Exit / Entrance	37 Concrete Washout, other pollution Issues
10 Temp Sediment Filter Bag / Dewatering	24 Temporary Stream Crossing	38 Berm (soil, riprap, rock)
11 Polyethylene Sheeting	25 Turbidity Barrier / Silt Boom	39 Gabion
12 Machined Rip Rap	26 Temporary Stream Diversion	40 Sheet Piling
13 Geotextile	27 Preserve Natural Resource / Buffer Zone	41 Haul Road
14 Permanent Seeding with Mulch or Sod	28 Mineral Aggregate Base on Subgrade	42 Bridge Construction

CONDITION CODES

M	Maintenance
U	Upgrade Needed (Failure Noted)
R	Replacement Needed
FM	Future Maintenance
C	Cleaning Needed
I	Increase Measures
W	Too Wet to Work Conditions
RO	Repeat Occurrence
SR	Sediment Release
FS	Final Stabilized
S	Stable (No Action Needed)
CM	Corrections currently being made
Other (O31): _____	
Other (O#2): _____	
Other (O#3): _____	

State/US Route or Road Name: Wolf River Blvd.TDOT Construction No.: 79954-3537-54

TDOT Contract No.: _____

Date 2/16/2012

Outfall Name or Station No. *(Existing Structure)	Rain Gage No.	Approx. Station No. From / To	LT, RT or Centerline	Date Last Disturbed	Date of Stabilization and Code T = Temp. P = Perm.	Existing EPSC Control Measure Codes*	Current Condition Codes*	Corrective Action(s) or Comments
* 109+51	2	East side of WRB	RT	2/13/2012		19,22	FM,W	Daily cleaning will be required, until further notice.
* 109+11	2	South side of Farmington	RT	2/13/2012		19,22	FM,W	Daily cleaning will be required, until further notice.
* 12+80	1	North side of WRB	LT	2/13/2012		19,22	FM,W	Daily cleaning will be required, until further notice.
	1	Walking Trail 36+00	LT	7/20/2011	T = 7-20-11	5,35	S,W	Temp. stable.
	1	Sta. 29+50 Slope	LT	7/20/2011	T= 9-01-11	16	S,W	Temp. stable.
	1 & 2	Sta. 13+40 - Sta. 107+75	LT, RT or CL	2/13/2012		30	FM,W	Haul roads dampened frequently for dust control, until further notice.
	2	76+50 - 103+46	RT	9/29/2011	T = 10-03-11	15,16,35	S,W	Temp. stable.
	2	92+50 - 107+00	LT	9/29/2011	T = 10-03-11	15,16,35	S,W	Temp. stable.
	1	6+75	LT	2/13/2012		19,22	FM,W	Daily cleaning will be required, until further notice.
	1	27+00	RT	10/3/2011	T= 10-03-11	15,16	S,W	Temp. stable.
	1	34+00	RT	8/25/2011	T= 8-25-11	16	S,W	Temp. stable.

EROSION AND SEDIMENT CONTROL MEASURE CODES

- | | |
|--|--|
| 1 Temporary Silt Fence / Filter Barrier | 15 Temporary Seeding with Mulch |
| 2 Temporary Diversion Berm or Ditch | 16 Temporary Mulch |
| 3 Temporary Slope Drain | 17 Erosion Control Blanket |
| 4 Rock Check Dams | 18 Flexible Channel Liner |
| 5 Brush Barrier | 19 Catch Basin / Storm Inlet Protection |
| 6 Sediment Removal | 20 Riprap Outlet Structure |
| 7 Straw Bale Check | 21 Riprap Energy / Velocity Dissipater |
| 8 Sand Bags | 22 Curb, Gutter, or Storm Sewer Protection |
| 9 Sediment Trap / Basin | 23 Temporary at Construction Exit / Entrance |
| 10 Temp Sediment Filter Bag / Dewatering | 24 Temporary Stream Crossing |
| 11 Polyethylene Sheeting | 25 Turbidity Barrier / Silt Boom |
| 12 Machined Rip Rap | 26 Temporary Stream Diversion |
| 13 Geotextile | 27 Preserve Natural Resource / Buffer Zone |
| 14 Permanent Seeding with Mulch or Sod | 28 Mineral Aggregate Base on Subgrade |

- | |
|---|
| 29 Excess Dirt Removed from Rdwy. Daily |
| 30 Haul Roads Dampened for Dust Control |
| 31 Ditch Liner |
| 32 Rock Silt Screen |
| 33 Temporary Silt Fence with Backing |
| 34 Enhanced Silt Fence |
| 35 Sediment Tube |
| 36 Sediment Dam |
| 37 Concrete Washout, other pollution Issues |
| 38 Berm (soil, riprap, rock) |
| 39 Gabion |
| 40 Sheet Pilling |
| 41 Haul Road |
| 42 Bridge Construction |

CONDITION CODES

- | | |
|----|--------------------------------|
| M | Maintenance |
| U | Upgrade Needed (Failure Noted) |
| R | Replacement Needed |
| FM | Future Maintenance |
| C | Cleaning Needed |
| I | Increase Measures |
| W | Too Wet to Work Conditions |
| RO | Repeat Occurrence |
| SR | Sediment Release |
| FS | Final Stabilized |
| S | Stable (No Action Needed) |

Other (O#1): _____

Other (O#2): _____

Other (O#3): _____



Old Name: Wolf River Blvd.

TDOT Construction No.: 79954-3537-54

TDOT Contract No.: _____

Date 2/16/2012


Outfall Name or Station No.	Rain Gage No.	Approx. Station No. From / To	LT, RT or Centerline	Date Last Disturbed	Date of Stabilization and Code T = Temp. P = Perm.	Existing EPSC Control Measure Codes*	Current Condition Codes*	Corrective Action(s) or Comments
	1	21+33 - 26+00	LT	2/2/2011	T = 10-6-11	15,16,33,35,41	S,W	Temp. stable.
	1	21+33 - 26+00	RT	10/10/2011	T = 10-6-11	15,16,35,41	S,W	Temp. stable.
	1	25+00	LT	12/14/2011	T = 10-6-11	15,16,33,35,41	S,W	Temp. stable.
	1	25+00	RT	9/29/2011	T = 10-6-11	15,16,33,35,41	S,W	Temp. stable.
	1	27+50	RT	10/6/2011	T = 10-6-11	15,16,33,35,41	S,W	Temp. stable.
	1	31+90	RT	9/29/2011	T = 10-6-11	15,16,35	S,W	Temp. stable.
	1	15+60	LT & RT	1/23/2012		15,16,33,35	FM,W	Headwalls are in place. Clean up and stabilize disturbed areas. No activity during visit.
* 108+37	2	North side of WRB	LT	2/13/2012		19,22	FM,W	Daily cleaning will be required, until further notice.
	1	23+00 - 26+00	RT	9/29/2011	T = 10-6-11	33,41	S,W	Temp. stable.
	1	25+00	RT	2/13/2012		15,33,35	FM,W	Remove sediment around existing trees in existing wetland. See photo

EROSION AND SEDIMENT CONTROL MEASURE CODES


CONDITION CODES

- | | | |
|--|--|---|
| 1 Temporary Silt Fence / Filter Barrier | 15 Temporary Seeding with Mulch | 29 Excess Dirt Removed from Rdwy. Daily |
| 2 Temporary Diversion Berm or Ditch | 16 Temporary Mulch | 30 Haul Roads Dampened for Dust Control |
| 3 Temporary Slope Drain | 17 Erosion Control Blanket | 31 Ditch Liner |
| 4 Rock Check Dams | 18 Flexible Channel Liner | 32 Rock Silt Screen |
| 5 Brush Barrier | 19 Catch Basin / Storm Inlet Protection | 33 Temporary Silt Fence with Backing |
| 6 Sediment Removal | 20 Riprap Outlet Structure | 34 Enhanced Silt Fence |
| 7 Straw Bale Check | 21 Riprap Energy / Velocity Dissipater | 35 Sediment Tube |
| 8 Sand Bags | 22 Curb, Gutter, or Storm Sewer Protection | 36 Sediment Dam |
| 9 Sediment Trap / Basin | 23 Temporary at Construction Exit / Entrance | 37 Concrete Washout, other pollution Issues |
| 10 Temp Sediment Filter Bag / Dewatering | 24 Temporary Stream Crossing | 38 Berm (soil, riprap, rock) |
| 11 Polyethylene Sheeting | 25 Turbidity Barrier / Silt Boom | 39 Gabion |
| 12 Machined Rip Rap | 26 Temporary Stream Diversion | 40 Sheet Piling |
| 13 Geotextile | 27 Preserve Natural Resource / Buffer Zone | 41 Haul Road |
| 14 Permanent Seeding with Mulch or Sod | 28 Mineral Aggregate Base on Sub grade | 42 Bridge Construction |


- | |
|----------------------------------|
| M Maintenance |
| U Upgrade Needed (Failure Noted) |
| R Replacement Needed |
| FM Future Maintenance |
| C Cleaning Needed |
| I Increase Measures |
| W Too Wet to Work Conditions |
| RO Repeat Occurrence |
| SR Sediment Release |
| FS Final Stabilized |
| S Stable (No Action Needed) |
| Other (O#1): _____ |
| Other (O#2): _____ |
| Other (O#3): _____ |

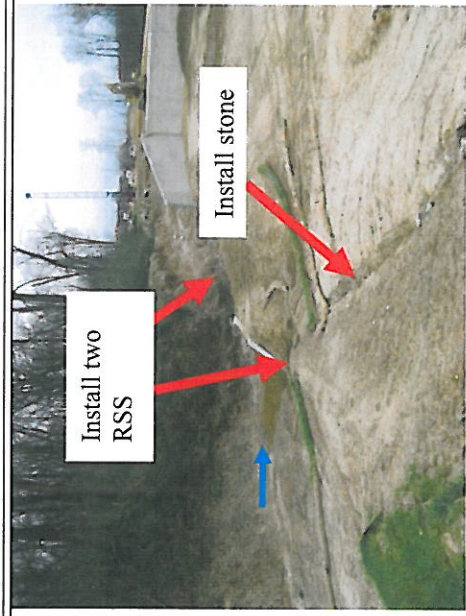

Outfall 1B Sta. 22+00 RT
Install two RSS's and stone as shown. (FM, W)

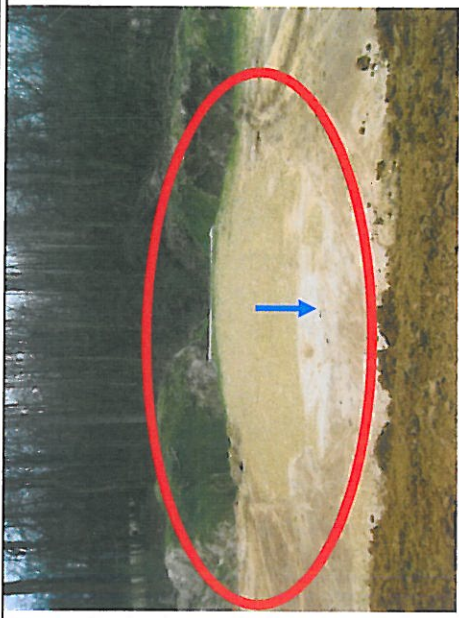

Outfall 10A & 10B Sta. 85+00 RT
Areas need to be temp. stabilized. (FM, W)

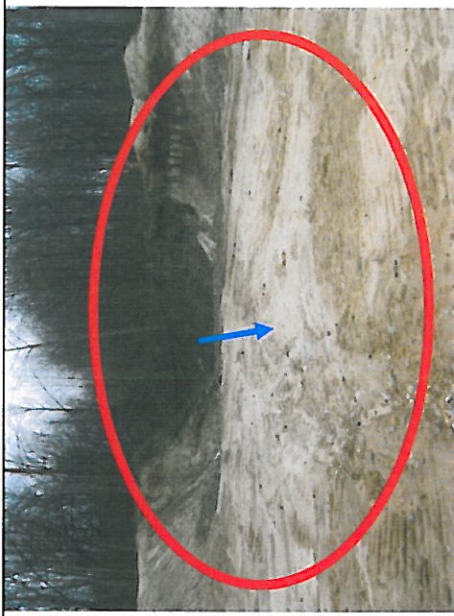

Outfall 11A Sta. 92+50 RT
Areas need to be temp. stabilized. (FM, W)



Sta. 25+00 RT
Remove sediment around existing trees in existing wetland. (FM, W)



City of Germantown
1920 S. Germantown Road
Germantown, TN 38138
